


AEVON

Accelerated Master Development Roadmap & Timeline


Planning basis: full-time / unrestricted development effort • 13 August 2026

This revised roadmap removes the previous two-hours-per-day constraint. It reflects an aggressive but realistic engineering plan for building AEVON toward a strong production system, while preserving architectural quality, approval controls and verification.

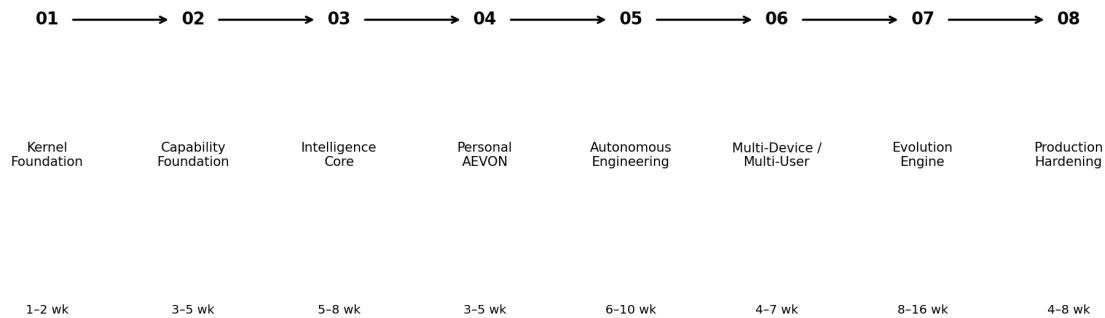

Primary planning target: approximately 12 months for a strong production AEVON, with an estimated practical range of **8–14 months**.

1. Executive Timeline

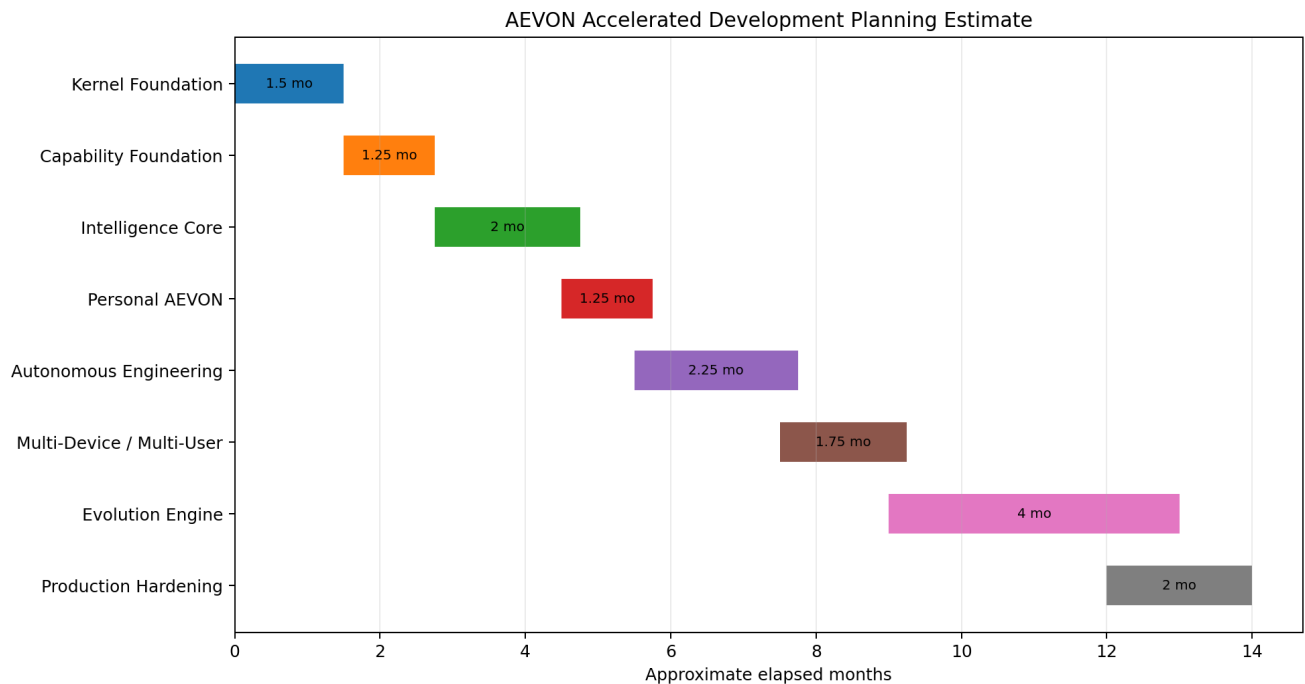

The timeline is a planning model, not a fixed deadline. Workstreams may overlap once their dependencies permit it. The later stages are expected to become faster as AEVON acquires reliable automation and autonomous engineering capabilities.

2. Development Stages

Stage	Planning range	Primary outcome
Kernel Foundation	1–2 weeks	Complete Kernel lifecycle, registry, event bus, health and required orchestration foundations.
Capability Foundation	3–5 weeks	Reusable capability/tool contracts, execution boundaries, permissions and approval mechanisms.
Intelligence Core	5–8 weeks	Intent understanding, context, reasoning, planning and controlled execution loops.
Personal AEVON	3–5 weeks	Memory, preferences, personalization and voice interaction.
Autonomous Engineering	6–10 weeks	Self-analysis, research, proposal, approved implementation, testing and verification.
Multi-Device / Multi-User	4–7 weeks	Identity, device awareness, personal/shared contexts, routing and synchronization.
Evolution Engine	8–16 weeks	Continuous self-analysis and improvement proposals under owner approval.
Production Hardening	4–8 weeks	Security, reliability, recovery, rollback, testing and safe upgrade mechanisms.

3. Milestone Targets

~3–5 months — **Usable AEVON**: A dependable application able to understand requests, invoke capabilities, maintain relevant context and execute approved tasks.

~5–8 months — **Strong Personal AEVON**: Personal memory, voice, richer reasoning, broader capabilities and meaningful multi-device foundations.

~8–14 months — **Production AEVON**: A robust system with autonomous-engineering foundations, multi-user/device operation, self-analysis and strong reliability/security controls.

~12–24+ months — **Full long-term vision**: AEVON evolves toward the broader ecosystem described in the project vision, where it can acquire or create new capabilities and continuously propose improvements to itself.

4. The Strategic Shift

The objective is not to manually implement an enormous fixed feature list. The highest-value milestone is making AEVON capable of extending its own capabilities safely.

Manual-development model

Request → human designs feature → human codes → human tests → integrate.

Target AEVON-development model

Request → AEVON understands intent → detects missing capability → researches options → designs a proposal → **owner approval** → implements → tests → verifies → integrates → records the change.

5. Non-Negotiable Self-Improvement Control

AEVON must never silently modify itself. It may analyze itself, identify limitations, research solutions, design changes and prepare implementations. Actual self-modification remains gated by explicit owner approval.

This principle is central to the architecture because increasing autonomy must not come at the cost of owner control, traceability or system integrity.

6. Engineering Strategy

Speed will come from good architecture, reusable packages/libraries, automation, testing and eventually AEVON's own engineering capabilities—not from skipping verification.

Every significant checkpoint should continue to follow: **implement** → **compile/test** → **behavioral validation** → **inspect diff** → **commit** → **push** → **update documentation** → **proceed**.

7. Current Position

Current era: Platform Foundation

Current architectural focus: Kernel Foundation

Immediate path: complete and verify the Kernel layer before moving into Capability Foundation.

8. What Could Change the Timeline

The estimate can move in either direction. Major accelerators include reusable frameworks, reliable automation, strong testing infrastructure and AEVON's eventual ability to assist with its own engineering. Major risks include architectural rework, security/reliability defects, integration complexity, unclear requirements and expanding scope.

Therefore, **12 months is the planning target, not a promise**. The 8–14 month range is the practical target for a strong production system under an aggressive development effort.

Architect's note: We should optimize for reaching the self-improvement loop correctly, not merely for reaching a calendar date. AEVON's ability to safely accelerate its own development is one of the most important multipliers in the entire project.
